



SP22-9

WWP EMERGENCY POWER GENERATOR AND ELECTRICAL SWITCHGEAR



CONSTRUCTION 0% | START DATE: 9/4/2024 | COMPLETION DATE: 4/21/2026

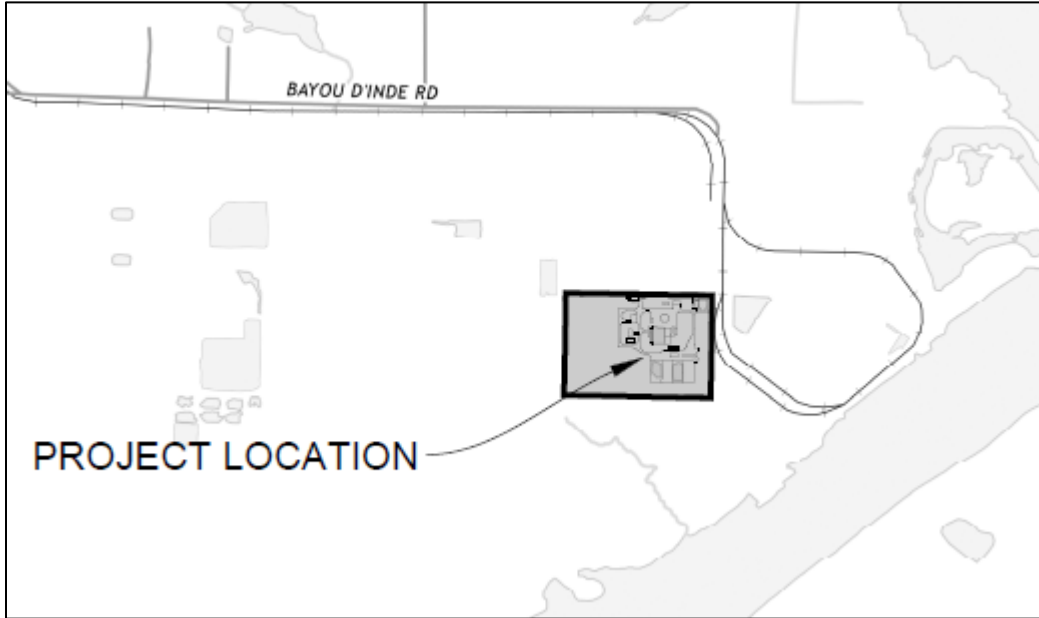

Engineer: Meyer & Associates Inc.
Cost Estimate: 2,200,000
Bid Date: 8/8/2024
Notice of Award: 8/13/2024
Bid Award Amount: 3,089,900.00
Contractor: Kaough & Jones Electric Co, Inc.
Notice To Proceed: 9/4/2024
Est. Sub. Completion Date: 4/21/2026
Actual Completion Date: TBA

SCOPE OF WORK

The project will consist of replacement of existing damaged 2,500 kW generator with two 1,500 kW generators.

